Bantu e.V.

BANTU E.V. · UGANDA

Cerebral palsy EDIRI pilot project

Progress report June to September 2023

Mbarara and surrounding districts, south-western Uganda



Primary health care workers and facilitators after the training workshop.

38

children reached through home follow-up

26

primary health care workers trained

35

hospital staff sensitized

EDIRI · P 23/91 · 2023

At a glance

From June to September 2023, the EDIRI pilot project brought early support for children with cerebral palsy closer to families in south-western Uganda. The partnership between OURS, Anchored Bridges Initiatives and Bantu e.V. combined home follow-up, health worker training, community outreach and radio awareness. Home visits reached 38 children, and parents in Rwampara formed a support group to share knowledge and advocate for their children.

Delivery compared with the target



Target: 40 people for each activity

Figures describe different activities and must not be added together as a total number of people.

3
community outreaches

1
parent support group formed

4 months
pilot implementation

Source: the figures and narrative in the original report.

Project profile

Implementation period	1 June to 30 September 2023
Contractual partner	Ruharo Mission Hospital
Implementing partner	Organised Useful Rehabilitation Services (OURS)
Partnership organisations	Anchored Bridges Initiatives (ABI) and Bantu e.V.
Project number	P 23/91 (Stiftung Nord-Süd-Brücken, EZ-Kleinprojektefonds, with funds from the BMZ)
Original report	Aaron Ndyowaawe, Programme Administrator, OURS, 9 November 2023

Project context and reported reach

Organised Useful Rehabilitation Services (OURS) is a community-based rehabilitation and inclusive development programme founded by Ankole Diocese in 1995 and operating under Ruharo Mission Hospital. Its services support children aged 0 to 18 with neurological and physical disabilities in south-western and western Uganda and neighbouring countries.

At the time of the pilot, OURS reported providing rehabilitation services to more than 3,000 children annually and registering over 500 new children each year, 40.3% of whom had cerebral palsy. The EDIRI pilot focused on children aged 0 to 5 and sought to improve access to early detection, identification, referral and interventions through support for children, caregivers, health workers and community structures.

Community stakeholders and local leadership

Two inception meetings in Rwampara District and Mbarara City North brought together 40 community stakeholders, meeting the planned target. Participants included 23 men and 17 women drawn from community development offices, police family protection units, probation services and local political leadership.

The meetings introduced the pilot and promoted the inclusion of children with cerebral palsy. Local authorities asked the project team for an updated list of children with disabilities in their communities so that local government structures could better identify where support was needed.



Aaron Ndyowaawe presents the EDIRI project objectives to community stakeholders.



The OURS Programme Administrator briefs stakeholders on rehabilitation services.



Rwampara District Chairperson Richard Owomugasho addresses the inception meeting.

Primary health care worker training

One workshop brought together 26 primary health care workers from health facilities in Mbarara City North and Rwampara District. Nine men and 17 women participated, representing 65% of the target of 40 health workers. Sessions addressed early detection, identification, referral and interventions for children with cerebral palsy.

Participants worked in groups to discuss issues affecting early identification and access to care. Attendance fell below target because the workshop coincided with government programmes, and the four-month implementation period left limited scope to arrange further training.




Primary health care workers and facilitators after the training workshop.



Health workers discuss early identification and barriers to care in small groups.



The Assistant District Health Officer for Rwampara delivers closing remarks.

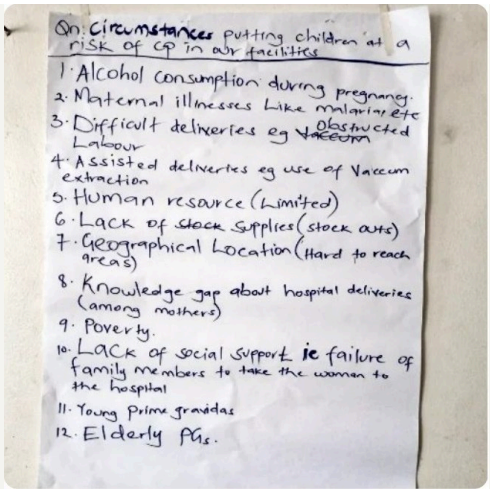

Workshop participants recorded issues raised during group discussion.

Home support and assistive devices

The project completed all planned home follow-up visits, reaching 38 children with cerebral palsy. Therapists worked with caregivers and other household members on practical ways to support children in activities of daily living. Home-based health education also addressed gaps in knowledge about care and rehabilitation.

The visits highlighted the need for regular follow-up and practical training within children's own homes and communities. Continued support would help caregivers build on the skills introduced during the pilot.

The project procured cerebral palsy seats and crutches, together with soft balls, blocks, toy shakers and building blocks for therapy. These items were intended to support functioning, mobility and independence.



A caregiver and therapist support a child during a home follow-up visit.

Community outreach and radio awareness

All three planned community outreaches took place: one in Rwampara and two in the neighbouring districts of Isingiro and Rukungiri. Radio programming accompanied the outreach work to raise awareness of disability, cerebral palsy and the value of early support.

The team reported increased demand from parents and caregivers seeking early interventions after the outreach activities. Parents from Rwampara and surrounding areas formed a support group for advocacy, lobbying and knowledge sharing. The team identified interest in establishing further groups if additional support became available.



A physiotherapist leads health education for caregivers during community outreach.



The programme social worker facilitates a group counselling session during outreach.



Project staff discuss cerebral palsy and early support during a radio broadcast.



Project staff take part in a community radio discussion.

Hospital staff sensitization

Hospital sensitization sessions took place at Devine Mercy Hospital and Mbarara Community Hospital on 15 and 21 August 2023. The sessions reached 35 of the 40 intended health workers, or 87.5% of the target, and addressed early identification and interventions for disabilities, including cerebral palsy.

Participants recommended a clear referral pathway and follow-up plan shared among stakeholders. They also requested similar sessions for the nursing schools attached to the institutions. The limited implementation period constrained the number of staff reached.



Health workers attend a hospital sensitization session on early identification and referral.



Health workers and project facilitators after a hospital sensitization session in Mbarara.

Delivery against planned activities

Activity	Planned	Reported delivery
Stakeholder inception meetings	2 meetings, 40 people	2 meetings; 40 participants (23 men, 17 women)
Primary health worker workshop	1 workshop, 40 people	1 workshop; 26 participants (9 men, 17 women), 65% of target
Home follow-up	All planned visits	All planned visits completed; 38 children reached
Community outreach	3 outreaches	3 outreaches completed in Rwampara, Isingiro and Rukungiri, with radio programmes
Hospital sensitization	2 sessions, 40 people	2 sessions; 35 health workers, 87.5% of target
Assistive devices and therapy materials	Provision of items	CP seats, crutches and assorted therapy toys procured

Figures describe different activities and must not be added together as a total number of people.

Priorities for continued support

Community awareness and access

Knowledge gaps and stigma continued to affect children with cerebral palsy and their families. The team recommended sustained community awareness work, radio programming and outreach so that more families could recognise available support and seek services earlier.

Health worker capacity and referral

Further training for health workers, medical training institutions and community structures was identified as a priority. Participants called for practical referral and follow-up arrangements and for sensitization to extend to nursing schools.

Continuity of family support

Regular home follow-up and caregiver training would help families continue the work introduced during the pilot. The parent support group in Rwampara offered a basis for peer learning and advocacy, with scope for additional groups and wider geographical coverage as resources allowed.

Partnership outlook

The four-month pilot delivered home-based support to 38 children, completed the planned community outreaches and engaged community leaders and health workers in early detection and referral. OURS expressed its appreciation to ABI, Bantu e.V. and partners in Germany. The programme requested continued support, subject to available resources, to reach more children with cerebral palsy and their families.

The pilot within project P 23/91

The pilot phase described here ran from 1 June to 30 September 2023. Project P 23/91 as a whole was extended to 31 October 2023 and widened to the districts of Mbarara, Rwampara, Ibanda, Isingiro, Ntungamo and Rukungiri. By the end of the project, 172 children with cerebral palsy and other disabilities had received medical rehabilitation, more than the 150 planned. Total project costs were 5,352.20 EUR, of which 3,929.00 EUR came from Stiftung Nord-Süd-Brücken (EZ-Kleinprojektefonds, with funds from the BMZ) and 1,423.19 EUR from Bantu e.V.'s own funds (Bantu e.V. annual report 2023, international projects).

Acknowledgements

Organised Useful Rehabilitation Services and Ruharo Mission Hospital · Anchored Bridges Initiatives (ABI) · Bantu e.V. · Stiftung Nord-Süd-Brücken with funds from the Federal Ministry for Economic Cooperation and Development (BMZ)

Original report submitted by Aaron Ndyowaawe, Programme Administrator, OURS. Source record dated 9 November 2023. Edition for the website of Bantu e.V., November 2026. Children's faces in the photographs have been blurred to protect their privacy.

Bantu e.V.

Together, we build sustainable and empowered communities.

CONTACT

Bantu e.V.
Kameruner Str. 1
13351 Berlin
Postfach 120344, 10593 Berlin

info@bantu-ev.org
www.bantu-ev.org
+49 176 34213765

SUPPORT OUR WORK

www.bantu-ev.org

GLS Gemeinschaftsbank eG
IBAN DE47 4306 0967 1035 6810 00
BIC GENODEM1GLS

Amtsgericht Charlottenburg
VR 37606 B

> This edition presents the historical report in a new layout. Dates, qualifications and financial reporting status refer to the original reporting period.

Redesigned edition · 10 November 2026

Bantu-Vereinigung für globale Bildung, Gerechtigkeit und Zusammenarbeit e.V.

Finanzamt für Körperschaften I Berlin · Steuernummer 27/661/53393
